



2014 - Minnesota Flood Relief Grant Phase 3B (Freeborn SWCD)

Grant Award: \$55,010

Total Project Budget: \$55,846

Progress as of February 2021:

| Fund Type | Spent |
|--------------|-----------------|
| Grant | \$47,926 |
| Match* | \$0 |
| Other | \$48,428 |
| Total | \$96,354 |


**Includes minimum 25% local match*

Grant Period:

August 2016 - December 2020

Project Sponsor:

Freeborn SWCD

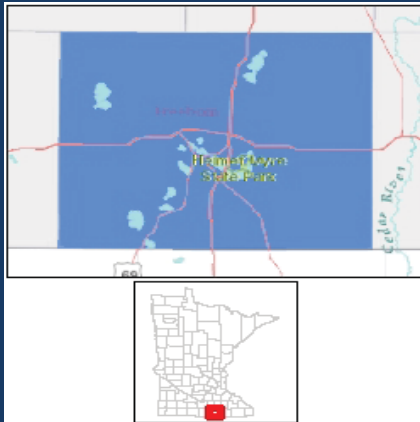

Project Contact:

Brenda Lageson
507-373-5607 x3
brenda.lageson@mn.nacdnet.net
<http://freebornswcd.org>

Pollution Reduction Estimates

| Indicator Name | Proposed | Actual |
|---|----------|--------|
| Phosphorus (Est. Reduction) (LBS/YR) | | 30.58 |
| Sediment (Tss) (TONS/YR) | | 34.93 |
| Soil (Est. Savings) (TONS/YR) | | 54.74 |

Actual Outcomes

As of 12/31/16 no funds were expended.

As of 12/31/17 no funds were expended.

Staff has been busy working with several landowners on DRAP list. It has been a difficult weather season and staff was wanting to complete projects in DRAP 1 & 2 first. We asked for and were granted an extension until 12/31/2019. 2018 staff hours are as follows.

Office Manager 1 hr. @ \$53.75, Manager 2 hours @ \$69.22, 3 Tech 43.5 hours @ 33.24 and 2 Tech 55 hours @ \$40.38.

The WASCOB has been nearly completed. The channel tile in the basin just needs to be installed. These BMP's installed just upstream of County Ditch 8 will prevent nutrients and sediment from getting directly into the ditch. This portion of the waterway is nearly completed. The support tile still needs to be installed along with getting some clean-up work done to make sure the field is ready to be farmed in 2020. These BMP's installed just upstream of County Ditch 8 will prevent nutrients and sediment from getting directly into the ditch.

All projects but one has been completed. This last one just needs some seeding touched up next summer 2021. The grant funds for the extra will be FY19.
